



भारत सरकार
GOVERNMENT OF INDIA

जल शक्ति मंत्रालय
MINISTRY OF JAL SHAKTI

जल संसाधन नदी विकास एवं गंगा संरक्षण विभाग
DEPARTMENT OF WATER RESOURCES, RD & GR

प्रधानमंत्री कृषि सिंचाई योजना (CADWM) कार्यक्रम के अंतर्गत गंग नहर आधुनीकरण फेज- II, राजस्थान की प्रथम प्रबोधन
प्रतिवेदन वर्ष 2026-27

FIRST MONITORING REPORT OF MODERNISATION OF GANG CANAL PHASE-II, RAJASTHAN UNDER PMKSY
(CADWM) for FY-2026-27



Latitude: 30.036376
Longitude: 73.758880
Elevation: 177.14±3.00 m
Accuracy: 3.54 m
Time: 18-05-2026 10:36:44
Note: 4Q

NoteCam @ iOS

केंद्रीय जल आयोग
CENTRAL WATER COMMISSION

यमुना बेसिन संगठन
YAMUNA BASIN ORGANISATION

प्रबोधन एवं मूल्यांकन निदेशालय, जयपुर (राजस्थान)
MONITORING AND APPRAISAL DIRECTORATE, JAIPUR (RAJASTHAN)

मई, 2026
May, 2026

MODERNISATION OF GANG CANAL PHASE-II, RAJASTHAN UNDER PMKSY (CADWM)

MONITORING REPORT AND STATUS REPORT

Period Of Monitoring Visit	:	18.05.2026 - 19.05.2026
Officers Participated	:	1. Shri Abhishek Gupta, Director, M&A, Jaipur 2. Shri Shakeel Ahmad, Assistant Director, M&A, Jaipur
Project Officials whom interaction was made	:	1. Shri N. L. Meena, SE, CAD 2. Shri Neeraj Kumawat, EE 3. Shri Ramniwas Man, EE 4. Shri Govardhan Meena, AE 5. Shri Ankur Kumar Raju. AE 6. Shri Raj Kumar Meena, JE Along with Other Field officers of CAD, GoR

CAD Works

1. Chak 76 LNP
2. Chak 4b
3. Chak 10Q-II
4. Chak 4Q

Contents

PART-I EXECUTIVE SUMMARY	1
1.1 PROJECT FEATURES:	1
1.2 Physical progress of CAD&WM Component:	2
1.3 ISSUES IN FOCUS:.....	2
1.4 OVERALL ASSESSMENT REGARDING PROJECT COMPLETION	3
Plate-I.....	4
Plate-II.....	5
Plate-III	6
PART –II STATUS OF CAD&WM COMPONENT	7
2.1 PROJECT SUMMARY	7
2.2 STRUCTURAL INTERVENTIONS AS BEING EXECUTED	8
2.3 NON-STRUCTURAL INTERVENTIONS AS BEING EXECUTED	8
2.4 CHANGE IN SCOPE IF ANY	8
2.5 ORGANISATIONAL SETUP FOR THE PROJECT	10
2.6 OVERALL ASSESSMENT REGARDING PROJECT COMPLETION	11
2.7 CONTRACTUAL ARRANGEMENTS	11
2.8 CONSTRUCTION SCHEDULING	11
2.9 PROGRESS OF STRUCTURAL INTERVENTIONS.....	11
2.10 QUALITY ASSESSMENT	12
2.11 PROGRESS OF NON-STRUCTURAL INTERVENTIONS	12
2.12 PHYSICAL PROGRESS/PROGRAM:	12
2.13 POINTS NEEDING ATTENTION	13
a. Points from previous monitoring report pending Compliances	13
b. Additional Observations during visit in May-26	14
2.14 BOTTLENECKS.....	14
ANNEXURE-I	15
ANNEXURE-II	18
ANNEXURE-III	19
ANNEXURE-IV	21
PHOTOGRAPHS.....	28
PART-III SUMMARY OF ACTIONABLE POINTS.....	36
3.1 CAD&WM WORKS:	36

PART-I EXECUTIVE SUMMARY

S. No.	Particulars	Name of Project	Cost of the Project	CCA
1	Original project	Gang Canal Phase-II	146.74 Cr	44,875 Ha
2	Revised project after merging phase-I and Phase-III with Phase-II	Gang Canal Phase-II	341.534 Cr (As per latest proposed MoU for FY 2026-27 Revised cost- Rs 328.062 Cr)	1,17,975 Ha

1.1PROJECT FEATURES:

The Gang Canal system lies in Sri Ganganagar district of Rajasthan. It was constructed during 1922-27 by Shri Ganga Singh Ji Maharaja of Bikaner State. It is operational since October, 1927. Bikaner canal is the part of this canal system. Except for Bikaner Canal which was lined with lime concrete, all other canals of this system were earthen. Due to improper maintenance, the lining of this canal was in highly dilapidated condition, reducing its carrying capacity from 2465 cusecs to only 2000 cusecs.

The project was started during the year 1982-83. Rajasthan State also made an additional allocation of 0.33 MAF to Gang Canal from its own share of surplus Ravi-Beas water. Due to additional allocation out of surplus water, at present 1.44 MAF water is being utilized for Gang Canal System through Bikaner Canal. A 76.20 Km. long Gang Canal Link Channel, connecting Indira Gandhi Nahar Feeder to Gang Canal with head discharge of 3230 cusecs (91.41 cumecs) is a part of this project.

The modernization project was approved by Planning Commission on 29-09-2000 for Rs. 445.79 Crore at 1998 price level. The latest estimate cost of the project (at 2008 price level) is Rs. 621.42 Crore (under AIBP), which was approved in the 106th TAC meeting held on 16-09-2010. Expenditure on the project is 677.15 Cr (630.65-work, 46.50-Estt) with outstanding liabilities of 0.345 Cr. The AIBP component of modernization project have been completed.

Government of Rajasthan scheduled to take up CADWM works on 44,875 Ha area in Gang Canal Phase- II which was commenced in 2015-2016 and was scheduled to be completed by 31.03.2017. Further, on the request of Government of Rajasthan, the GoI agreed to include the balance CCA of Gang Canal Phase I as well Gang Canal phase III (part of original Gang Canal) and approved the proposal with modified CCA 1,17,975 Ha and cost as Rs 341.534 Cr. Accordingly the MoU was extended up to 31.03.2022 by the Government of India. The project was originally scheduled for completion by March 2022. However, due to delays in implementation, the completion period was extended up to March 2026 as per revised MoU. As the project remains incomplete even after the extended timeline, the Command Area Development (CAD) Department has proposed a further extension of the project up to March 2027 through latest revised MoU for FY 2026-27 with revised total estimated project cost of ₹328.062 Cr.

1.2 Physical progress of CAD&WM Component:

Modified CCA and Latest Revised cost of Gang Canal Phase-II are 1,17,975 Ha and Rs 328.062 Cr respectively. CCA of 112353 Ha with a qualified eligible expenditure of Rs. 304.95 Crore has been incurred in Gang Canal Phase-II till 30.04.2026. CA amounting to **Rs. 150.4198 Cr** has been utilized by project up to **31.03.2026**, and an additional **token CA of Rs. 1.29 Cr** has been released for **FY 2026–27**. Total of 180 No's of Water User Associations (WUAs) have been created and functioning in the whole Gang Canal System (314268 Ha). Details physical and financial progress is enclosed at **Annex-IV**.

1.3 ISSUES IN FOCUS:

1. Progress of distribution of functional grant to WUA is slow. Functional grant has been distributed only for 66405 Ha out of 117975 Ha upto April 2026.
2. As per the latest MoU, total cost of the project is fixed at Rs 328.062 Cr for covering CCA of 117975 Ha by Mar-2027. Qualified eligible expenditure up to 31.03.2026 is Rs 304.95 Cr with physical progress of 112353 Ha. In the CA proposal, Plan for 2026-27 has been kept for covering balance CCA of 5622 Ha with an estimated cost of Rs 22.31 Cr. Central assistance for FY 2026-27 has been calculated considering ceiling cost of project as 328.062. Cr as per latest MoU. Cost over and above the ceiling cost (Rs 328.062 Cr) if any shall be entirely borne by the states as per Clause 4.4 of the “Guidelines for Central Assistance for Command Area Development Works in Prioritized AIBP Funded Irrigation Projects” for completion of the project.
3. Ceiling of establishment cost had been fixed at 10 percent of OFD works as per CADWM guidelines.

4. Third-party concurrent evaluation reports of project for previous financial years have not been submitted and still pending.


1.4 OVERALL ASSESSMENT REGARDING PROJECT COMPLETION

Progress in non-structural component is extremely slow and necessitates intervention of CE, CAD -Bikaner and CE, CAD (Additional Secretary) for expediting the progress. Progress in structural component is approximately 95.23%, **however progress in non-structural component is only 56.29 %**. Further, it necessitates regular monitoring and supervision by senior officers so that the project is not delayed further as any delay will cause subsequential denial of benefits to the stakeholders.


MODERNISATION OF GANG CANAL, SRI GANGA NAGAR, RAJASTHAN

(LOCATION MAP OF SRIGANGANAGAR)



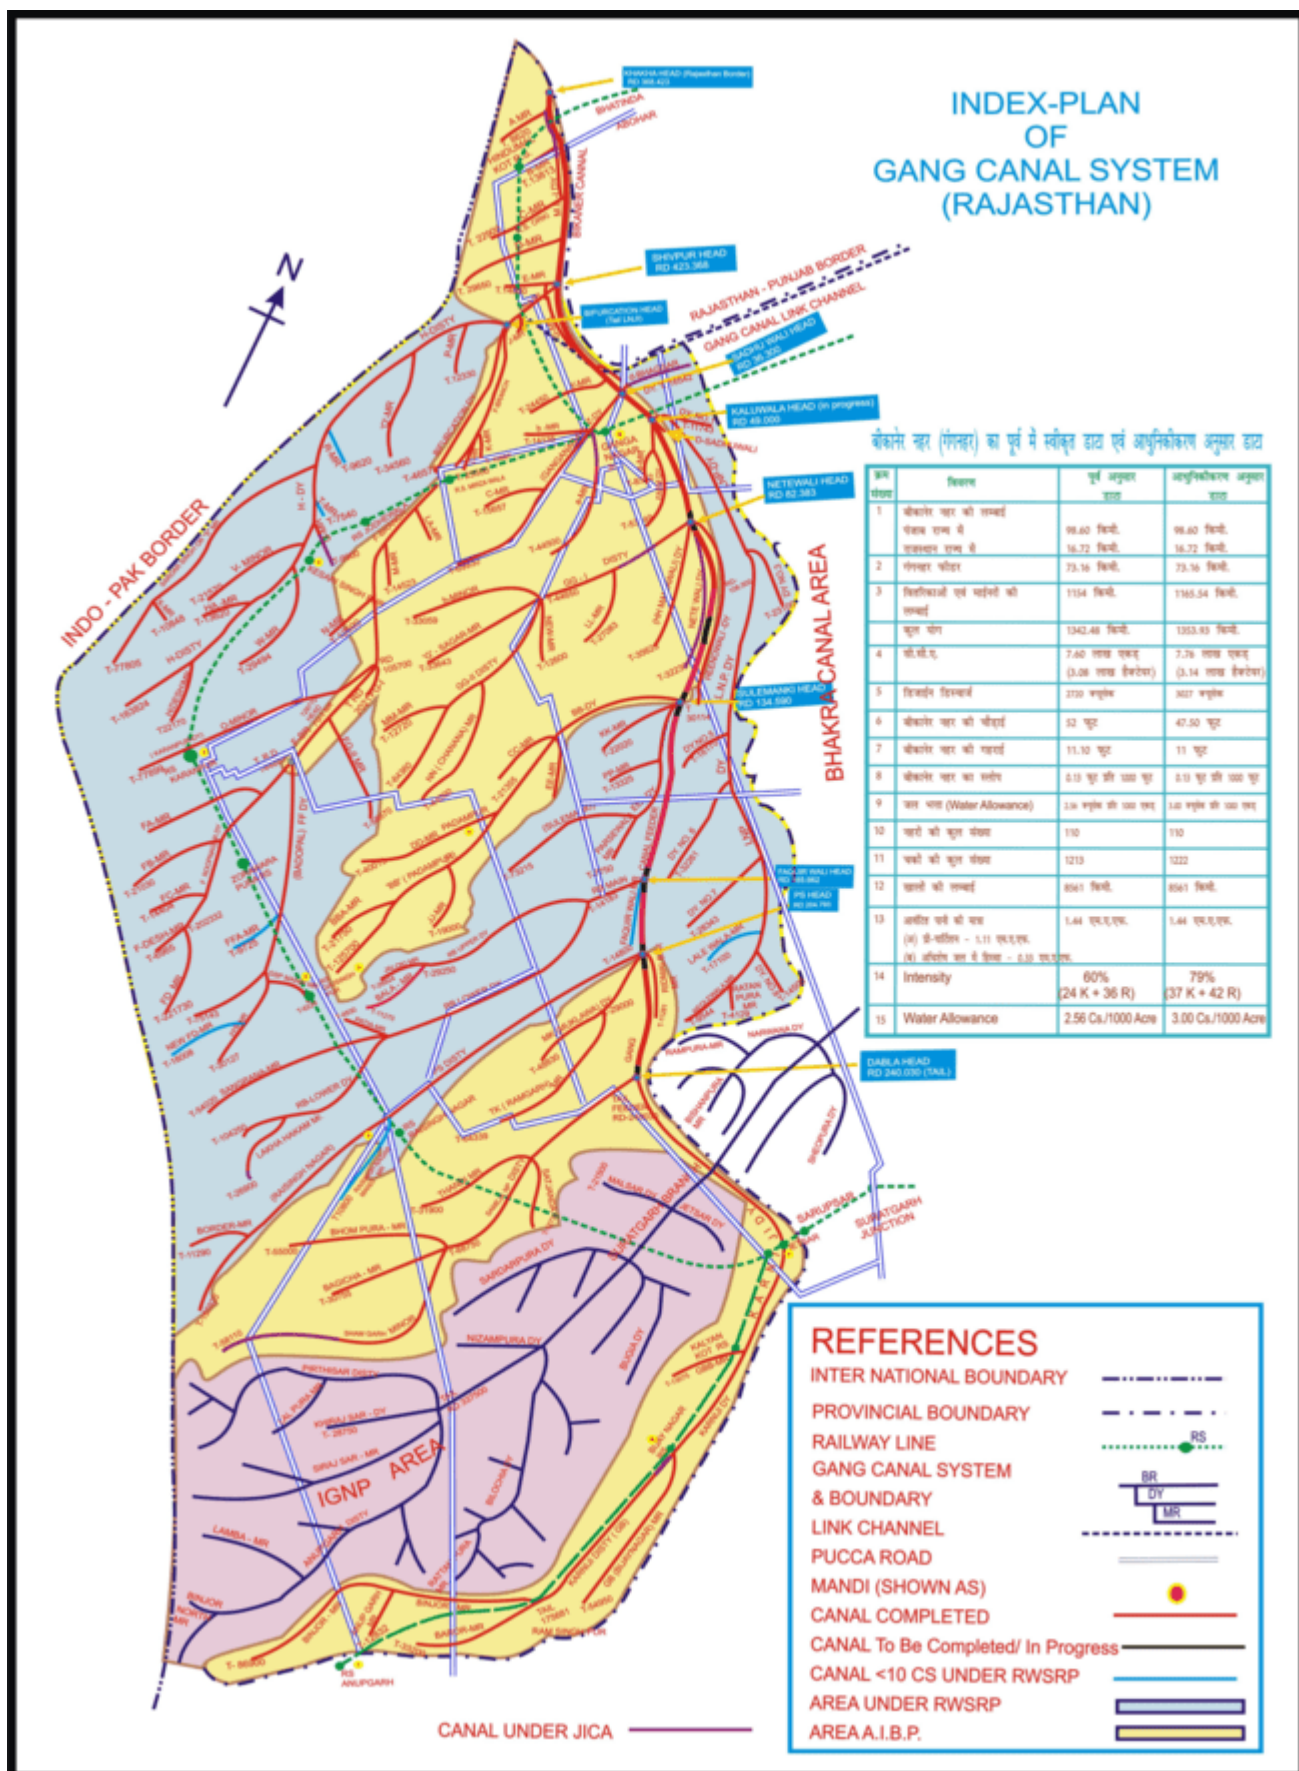

Line Diagram (Gang Canal Feeder)

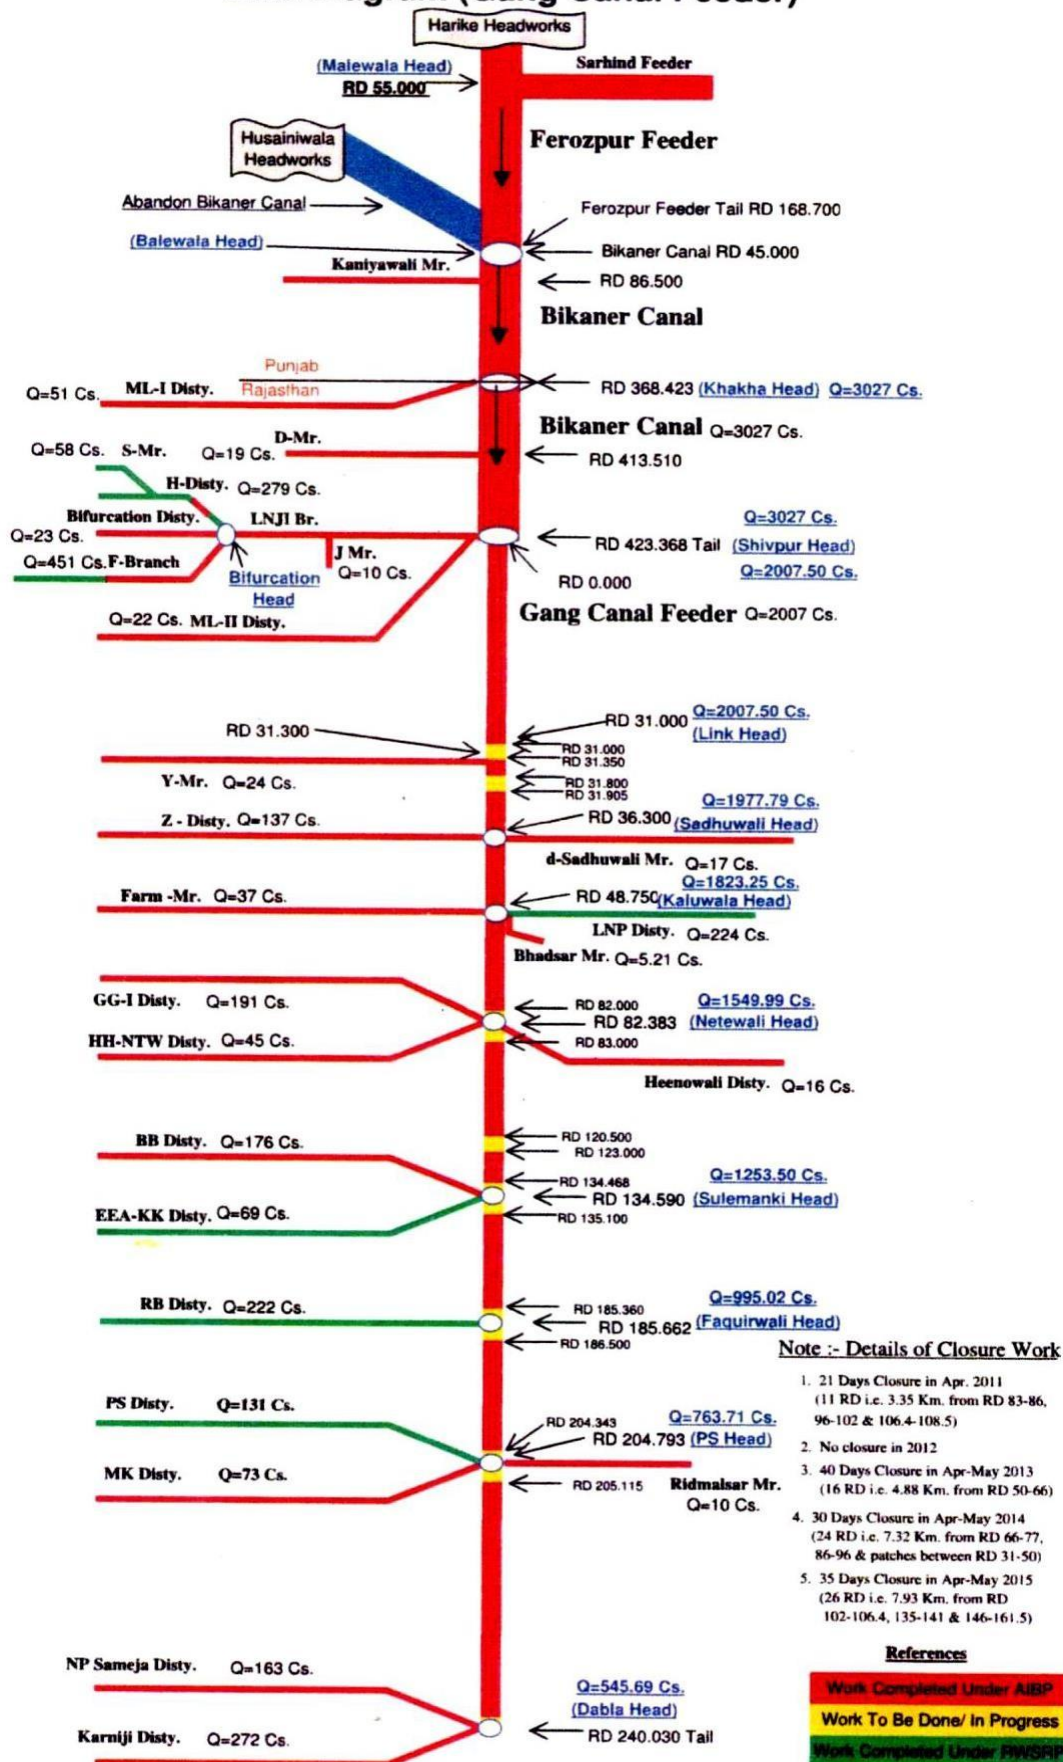

PART –II STATUS OF CAD&WM COMPONENT

2.1 PROJECT SUMMARY

Government of Rajasthan scheduled to take up CADWM works on 44,875 Ha area in Gang Canal Phase- II which was commenced in 2015-2016 and was scheduled to be completed by 31.03.2017. Further, on the request of Government of Rajasthan, the GoI agreed to include the balance CCA of Gang Canal Phase I as well Gang Canal phase III (part of original Gang Canal) and approved the proposal with modified CCA 1,17,975 Ha and cost as Rs 341.534 Cr. Accordingly the MoU was extended up to 31.03.2022 , 31.03.2024 and further extended upto March 2026, which was accepted by DoWR, RD&GR with revised total cost of Rs. 340.842 Cr. But project is still not completed by project authorities by Mar-2026 due to various constraints . In this regard, a revised MoU for further extension of the project upto March-2027 has been proposed by WRD.

The details of Gang Canal Phase- II are as below:

Name of Project	CCA	Funds Released / Date	Physical Progress as on 30.04.2026	Physical Progress (in %)	Total Eligible Expenditure upto 30.04.2026
Gang Canal Phase-II	44,875 Ha (Revised 117975 Ha)	Rs 10.00 Cr / 29.01.2016	Field channel works 112353 against 117975 Ha	95.23 %	Rs 304.95 Cr
		Rs 2.479 Cr / 04.01.2018-			
		Rs 7.43 Cr / 11.12.2018-			
		Rs 10.22 Cr / 08.11.2019	Functional grant to WUAs 66405 Ha out of 117975 Ha	56.29 %	
		Rs 14.87 Cr / 24.09.2020			
		Rs 9.37 Cr / 03.03.2021			
		Rs 33.71 Cr/ 24.12.2021			
		Rs 13.648 Cr/ 02.03.2022			
		Rs 12.3609 Cr / 30.11.2022			
		Rs 11.06 Cr / 09.08.2023			
		Rs 11.06 Cr/ 13.03.2024			
		Rs 1.9071 27.01.2025			
		Rs 12.879 Cr/ 24.09.2025			

		Rs. 1.29 Cr/ 27.03.2026			
--	--	----------------------------	--	--	--

2.2 STRUCTURAL INTERVENTIONS AS BEING EXECUTED

The structural interventions related to Gang Canal Phase-I and II include survey and planning, lining of field channels. Govt. of Rajasthan requested for exemption of 10% Micro irrigation in July 2019. Director M&A Jaipur and Dy Director M&A Jaipur visited the project in the month of August 2019 for the assessment of ground situation. On the basis of field visit and recommendation of M&A Dte Jaipur, Govt. of Rajasthan was accorded exemption of mandatory 10% Micro-Irrigation on ground situations by MoJS, Govt. of India. However, no component under correction of system deficiencies, reclamation of water-logged areas has been taken.

2.3 NON-STRUCTURAL INTERVENTIONS AS BEING EXECUTED

Non-structural interventions proposed for execution includes onetime functional grant to WUAs. Functional grant has been distributed only for 66405 Ha out of 117975 Ha upto April 2026. The overall progress of the project remains slow, with only 56.29% of the work completed. The pace of implementation requires focused attention and close monitoring by senior officers of the Government of Rajasthan to ensure timely completion of the balance works and achievement of the project completion target of March 2027, as committed by the State Government in the latest revised MoU.

2.4 CHANGE IN SCOPE IF ANY

The command area development works of Gang Canal Project was scheduled to be carried out in 3 Phases. Gang Canal Phase-I and Gang Canal Phase –II were already under execution. Rs. 61.19 Cr were released to Gang Canal Project Phase-I on 29.03.2016 and Rs 10.00 Cr were released to Gang Canal Phase-II on 29.01.2016. Subsequently, an amount of Rs 2.479 Cr on 04.01.2018, Rs 7.43 Cr on 11.12.2018, Rs 10.22 Cr on 08.11.2019, Rs 14.87 Cr on 24.09.2020, Rs 9.37 Cr on 03.03.2021, 33.71 Cr on 24.12.2021, 13.648 Cr on 03.03.2022, Rs 12.3609 Cr on 30.11.2022, Rs 11.06 Cr on 09.08.2023 and Rs.11.06 Cr on 13.03.2024, Rs. 1.9017 Cr on 27.01.2025, Rs. 12.879 Cr on 24.09.2025 and Rs. 1.29 Cr on 27.03.2026 were released to Gang Canal Phase-II. Therefore, cumulative Central Assistance (CA) amounting to Rs.152.2467 Cr has been released up-to 30.04.2026 to Gang Canal Project Phase-II.

During the meeting held on 17.08.2017 under the chairmanship of Commissioner (CAD), SJC (CAD), MoWR, RD & GR informed that in the cabinet note approved for PMKSY in July 2016 only 45,694 Ha of Gang Canal Project has been included. It was therefore decided that Gang Canal Phase-II will be taken up under existing CADWM scheme of MoWR, RD & GR and the balance CCA of Gang Canal Phase-I and full CCA of Gang Canal Phase-III will be taken up under the other scheme. The minutes of the meeting are at **Annexure-I**.

Gang Canal Phase-II commenced in 2015-16 and was scheduled to be completed by 31.03.2017. However, till 31.03.2017 CAD works for 8252 Ha with expenditure of Rs. 11.77 Crore could be achieved. The cost of project also got revised to Rs. 134.78 Cr from earlier approved cost of Rs.146.74 Cr. Therefore, a revised MoU for seeking extension of project upto 31.03.2019 with balance CCA of 36,623 Ha and cost of Rs. 123.01 Cr was submitted by GoR to MoWR, RD & GR, GoI. Further, the MoU was updated in 2019 and extended upto 31.03.2021. Further, on the request of Government of Rajasthan, the GoI agreed to include the balance CCA of Gang Canal project Phase I as well Gang Canal project phase III (part of original Gang Canal). The GoI approved the proposal vide order dated 31.12.2019 with CCA modified to 117,975 Ha and cost as Rs 341.534 Cr. Accordingly, the MoU was updated and extended upto 31.03.2022 by the Government of India. The project was originally scheduled for completion by March 2022. However, due to delays in implementation, the completion period was extended up to March 2026 as per revised MoU. As the project remains incomplete even after the extended timeline, the Command Area Development (CAD) Department has proposed a further extension of the project up to March 2027 through latest revised MoU for FY 2026-27 with revised total estimated project cost of ₹328.062 Cr.

Govt. of Rajasthan requested for exemption of 10% Micro irrigation in July 2019. Director M&A Jaipur and Dy Director M&A Jaipur visited the project in the month of August 2019 for the assessment of ground situation. On the basis of field visit and recommendation of M&A Dte Jaipur, Govt. of Rajasthan was accorded exemption of mandatory 10% Micro-Irrigation on ground situations by MoJS, Govt. of India.

As per previous MoU, signed in 2020, 522 Chaks/outlets were included having total CCA of 117,975 Ha. As per State Government, CCA of outlet 68 LNP was declared bifurcated into two i.e., 68 LNP-A and 68 LNP-B, making total outlets to 523. Further, In the revised

MoU for extension of project up to March 2024, 24 Chaks/outlets having CCA of 3976 Ha are removed and the actual executed / executable CCA was calculated for balance 499 Chaks/outlets, and a saving of 5004 Ha was arrived at. Apart from it, 39 new outlets having CCA of 8980 Ha, which were declared unserviceable by the Zila Parishad recently, have also been included. Thus, as per State Government, the modified scope of the project GCP-Phase II is to cover 538 Chaks/outlets having a CCA of 117975 Ha. Further in the proposal of revised MoU (2024-2026), 14 no's of existing chaks (out of 538) having area of 1147 Ha has been deleted citing unavailability of NAKARA certificates from Zila Parishad and additional 41 no's of chaks of old Gang system having area of 8080 ha has been added. Actual executed CCA of completed chaks were determined against the provision taken in the MoU of 2022-24 and net saving of 6933 ha has been arrived at by project authorities, thus keeping the total CCA in the revised MoU (24-26) as 117975 Ha. Revised MoU has been accepted by DoWR, RD & GR with revised total cost of Rs. 340.842 Cr.

Further, for achieving the originally proposed command area of 1,17,975 Ha, the Government of Rajasthan (GoR) has submitted a revised proposal under the latest MoU (submitted upto 2027). The balance area of 5,622 Ha could not be completed due to the non-feasibility of 17 chaks covering 3,743 Ha and ongoing works covering 1,879 Ha beyond 31.03.2026. To achieve the original target, GoR has proposed 20 new chaks covering 3,939 Ha, along with the ongoing works of 1,879 Ha, totaling 5,818 Ha, in replacement of the remaining 5,622 Ha, with completion targeted by 31.03.2027. Further, the project cost has been revised downward to Rs. 328.062 Cr from Rs. 340.842 Cr approved under the MoU (2024–26).

2.5 ORGANISATIONAL SETUP FOR THE PROJECT

The administrative Department at the State Level is CAD and Water Utilization (CAD&WU) Department headed by Principal Secretary. At the project level, it is headed by the Area Development Commissioner based at Bikaner. The Area Development Commissioner's office of CADA (Command Area Development Authority) is responsible for all other development works. The area Development Commissioner is assisted by an Additional Area Development Commissioner (HQ) as second in command and for Jaisalmer, Additional Commissioner-cum Secretary (Mandi Development committee). Chief Engineer (West), CAD Bikaner is responsible to carry out all construction activities. Chief Engineer is assisted by 4 SE rank officer further supported by 8 Nos. Executive Engineers and 1 Chief Account Officer. The organization chart is at **Annexure-II**.

2.6 OVERALL ASSESSMENT REGARDING PROJECT COMPLETION

Monitoring team of CWC, Jaipur visited the various sites under the project during 18th -to 19th May 2026. The details of the monitoring team, officers from the State Govt. present during the visit and the site visited are indicated at **Annexure-III**. Project was scheduled to be completed by March 2024. Project was not completed by March 2024, revised MoU for further extension of the project upto March 2026 was proposed by CAD, which was accepted by DoWR, RD&GR with revised cost of Rs. 340.842 Cr. Project is still not completed by March 2026, therefore, revised MoU for further extension upto March 2027 is submitted by CAD.

2.7 CONTRACTUAL ARRANGEMENTS

Calculation of quantities and estimation of cost and contracts are done chak- wise. Chak has an area between 100-300 Ha; however, the area may further vary. Work is awarded to the successful tenderer. It is noticed that the tenders are generally less than 1 Crore and are approved at the level of Executive Engineer or at Superintending Engineer level.

2.8 CONSTRUCTION SCHEDULING

Total CCA under Gang Canal Phase-II is 1,17,975 Ha. The Irrigation intensity proposed after modernization is 79%. The irrigation potential is therefore 93,200 Ha (79% of 117975 Ha). The project authorities have proposed to develop field channels as below as per revised MoU:

Sl. No.	Year	Field channels developed/proposed to be developed (CCA in Ha)
1.	Till 23-24	102687
2.	2024-25	780
3.	2025-26	8886
4.	2026-27	5622
	TOTAL	117975

2.9 PROGRESS OF STRUCTURAL INTERVENTIONS

CCA of 112353 Ha with an eligible expenditure of Rs 304.95 Crore have been developed

in Gang Canal Phase-II till 30.04.2026. Central Assistance (CA) amounting to Rs 152.2467 Cr has been released to Gang Canal Phase-II up-to 30.04.2026.

2.10 QUALITY ASSESSMENT

The quality of work on the visited sites is found reasonable. Further no work was ongoing during the visit. On interaction at site, WUA presidents and farmers conveyed their satisfaction towards the undertaken work.

2.11 PROGRESS OF NON-STRUCTURAL INTERVENTIONS

As per provisions of Rajasthan Farmers Participation Act' 2000, a provision of 180 WUA'S was kept in Gang Canal System. All the WUA'S have been formed. These are functioning properly as per requirement of the system. The entire area of the project is covered under warabandi. This activity is being taken up by the WUA'S as per provision of Rajasthan farmer's participation Act.

Monitoring team of CWC, Jaipur interacted with WUA President/members/stakeholders of Chak 76 LNP, 10 Q II, 4b and 4Q.

S. No.	Chak	WUA representatives
1	76 LNP	Shri Hanuman Punia
2	4 b	Shri Gurupooran Singh Dhami and Manga Singh
3	10 Q II	Shri Pooran Chand and Vipin Saharan
4	4 Q	Shri Rajendra Beniwal

2.12 PHYSICAL PROGRESS/PROGRAM:

Physical Progress/Program:

S No	Activity	Total Quantity of Work Involved (Thousands Ha)	Cumulative Achievement Upto Mar-2026 (Thousands Ha)	Targets & Achievement for 2026-27		Cumulative Achievement Upto April 2026 (Thousands Ha)
				Targets for the year 2026-27 (Thousands Ha)	Achievements till 30.04.2026 (Thousands Ha)	
A	<u>Structural Intervention</u>					
a)	Survey, Planning and Design	117.975	112.698	5.277	0.0	112.698

b)	(i) Total area of Lined Channels /underground pipelines (in Th ha)	117.975	112.353	5.622	0.0	112.353
B	<u>Non-Structural Interventions</u>					
	(I)One Time Functional Grant	117.975	66.405	51.570	0.0	66.405

2.13 POINTS NEEDING ATTENTION

a. Points from previous monitoring report pending Compliances

1. State Government should take all necessary corrective measures to ensure completion of the project by **March 2027**. The physical progress under various project activities has not been achieved in accordance with the year-wise targets stipulated in the last MoU signed for the project. Furthermore, progress under the non-structural components remains very slow. As of **April 2026**, Functional Grant has been distributed for only **66,405 ha** against the total project area of **117,975 ha**, indicating significant shortfall in implementation.
2. During various monitoring visits, it has been observed that the entire Culturable Command Area (CCA) of several chaks is not being covered under the CADWM Project, and only portions of the chaks are being taken up for implementation. In this regard, the State Government is advised to map all field channels/watercourses constructed under the CADWM Project within the project command on GIS layers to facilitate a comprehensive assessment of command area coverage. Accordingly, complete details of all field channels/watercourses constructed till date, along with their corresponding GIS mapping and the extent of coverage of each chak, may be furnished to this office for verification, assessment, and evaluation of the actual command area covered under the Project.
3. As per Clause 14 of the latest MoU, State Government is required to carry out an independent evaluation of the project through an independent agency, and evaluation report is to be submitted to CWC/Ministry. State Government is, therefore, advised to undertake the independent evaluation, and furnish the evaluation report to CWC/Ministry at the earliest.
4. During the meeting held on **20.05.2025** in the office of Additional Chief Engineer (CAD), Bikaner, a demonstration of **CWC GeoCrop Application** was given, and the importance of collection and uploading of crop data for areas covered under CAD works was emphasized. Additional Chief Engineer assured that crop data for the ensuing

Kharif season would be uploaded in the application. Further, during the field visit to **Sri Ganganagar**, Superintending Engineer (SE), Executive Engineer (EE), and other departmental officials were also imparted training-cum-demonstration on the methodology for crop data entry in the application. The project authorities are requested to furnish the current status of crop data collection and updation in the CWCGeoCrop Application.

b. Additional Observations during visit in May-26

1. Progress towards release functional grant is lagging Structural/Non-Structural intervention needs to be expedited for completion of project by March-2027.

2.14 BOTTLENECKS

Progress towards release of functional grant is lagging. Structural / Non-Structural interventions of the project need to be expedited and requires attention of CE -CAD-Bikaner and CE-CAD & Additional Secretary to keep the progress aligned with scheduled targets.

Record of discussion of the Meeting held on 17.08.2017 regarding Gang Canal Project, Phase-I and Phase-II in the chamber of Commissioner (CAD), MoWR, RD & GR

**No.N.19011/4/2015-CADWM-509
Government of India
Ministry of Water Resources
River Development and Ganga Rejuvenation
(CADWM Wing)**

438, Krishi Bhawan,
New Delhi-110001


Dated the 29th August, 2017

Sub : Record of discussion of the Meeting held on 17/08/2017 regarding Gang Canal Project, Phase-I and Phase-II in the chamber of Commissioner(CAD), MoWR,RD&GR – reg.

Ref : Letter No.12/01/2017/M&A/CWC-Jaipur dated 18/08/2017.

Please find enclosed herewith minutes of the meeting held on 17/08/2017, approved by Commissioner (CAD) for further necessary action at your end. A soft copy of the same is also being sent via email.

Encl: As above.


(Vijai Saran)
Sr. Joint Commissioner (CAD-I)
☎ 011-23383090
Email : cadwmwm-mowr@nic.in

Director (M&A),
Yamuna Basin Organisation,
Central Water Commission, Room No.107,
Kendriya Sadan, Sector-10,
Vidhyadhar Nagar, Jaipur-302035.

Meeting held to discuss Modalities of Central Assistance to Gang Canal CAD Projects Phase-I & Phase-II, on 17.08.2017 at 11:00 Hrs in the chamber of Commissioner CAD, MoWR, RD & GR , Room No. 236 A, Krishi Bhawan, N. Delhi.

Brief Record of discussions

A meeting under the Chairmanship of Commissioner, CAD, MoWR, RD & GR, GoI was held in the Chamber of Commissioner (CAD), MoWR, RD & GR, on 17.8.2017, on request of Government of Rajasthan, to discuss modalities of Central Assistance to Gang Canal CAD Projects Phase-I & Phase-II and other issues on projects proposed to be included under the scheme of incentivisation being proposed to be undertaken shortly by MoWR, RD & GR. The list of participants is **annexed** herewith.

2. The Chairman welcomed the participants, and requested Director, M&A, CWC, to take up the agenda items. Director, M&A, CWC, Jaipur briefed the participants about the Gang Canal Phase-I and Gang Canal Phase-II projects of Rajasthan. It was informed that the total CCA of Gang Canal System is 3.14 thousand hectare, out of which about 0.69 thousand hectare was already developed before taking up the project under CADWM programme of MoWR, RD & GR. The details of progress for the same is tabulated below:

Name of Project	CCA (Ha)	Funds Released / Date	Physical Progress as on 31.03.17 (Ha)	Unspent balance as on 31.03.17 (Rs. In lakh)
Gang Canal Phase-I	1,18,252	Rs. 6119.89 Lacs / 29.03.2016	54010	928.19
Gang Canal Phase-II	44,875	Rs 1000.00 Lacs / 29.01.2016	8252	411.82
Gang Canal Phase-III	88,402	Project proposal examined and comments sent to GoR.	-	-


3. SJC, CAD, MoWR, RD & GR informed that in the Cabinet Note approved for PMKSY in July, 2016, only 45,694 ha CCA of Gang Canal Project has been included. After detailed deliberations the following were agreed upon:
 - i) In the given circumstances, the best course is to consider the 44,875 hectare proposed in Phase II to be under PMKSY. Accordingly, Government of Rajasthan will submit revised MoU and proposal for Central assistance for Gang Canal Phase – II for the

balance command under the existing scheme of CADWM, at the earliest. It was assured by Govt. of Rajasthan officials that the same would be submitted within a month.

- ii) The proposals for the balance CCA of Gang Canal Phase-I and full CCA of Gang Canal Phase-III will be taken up under the Scheme of Incentivisation for Bridging Irrigation Gaps (**ISBIG**) along with the rest of Projects of GoR posed for funding. The formal request in this regard will be made by GoR in this regard.
- iii) Utilization Certificates for the entire funds released earlier in respect of Gang Canal Phase-I and Phase-II may be submitted by Government of Rajasthan at the earliest.

Meeting ended with a vote of thanks to the chair.

Organizational Setup

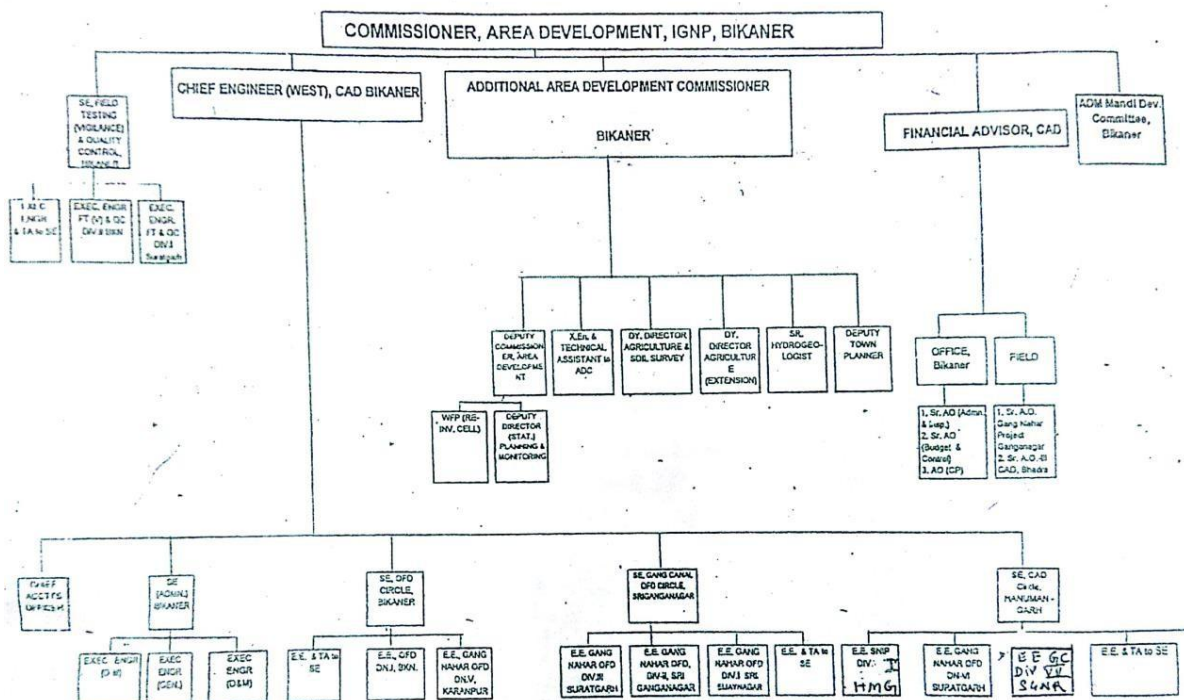

Details of Site Visit

The monitoring visit was done by team of Monitoring and Appraisal Directorate, CWC, Jaipur during 18-19 May, 2026. This is First visit of the Project during Financial Year 2026-2027. The following CAD components and other places of the project were visited:

- a) **Chak 76 LNP:** The total Culturable Command Area (CCA) of the Chak is 86.72 ha, and the entire 86.72 ha has been considered as the effective CCA under the CADWM Project. The construction of the water course has been completed; however, it has not yet been handed over to the Water Users Association (WUA). The total length of water courses in the Chak is 2,263.14 m, and the entire length of 2,263.14 m has been constructed under the scheme (Chak plan attached).
- b) **Chak 10 Q II:** The total CCA of the Chak is 213.42 ha, and the effective CCA considered under the CADWM Project is 147.05 ha. The construction work is completed, and the water course has been handed over to the WUA. The total length of water courses is 5532.12 meters, of which 3520.44 meters have been constructed under this scheme (Chak plan attached).
- c) **Chak 4 b:** The total Culturable Command Area (CCA) of the Chak is 323.59 ha, and the entire 323.59 ha has been considered as the effective CCA under the CADWM Project. The construction of the water course has been completed and has been handed over to the Water Users Association (WUA). The total length of water courses in the Chak is 7,709.30 m, and the entire length of 7,709.30 m has been constructed under the scheme (Chak plan attached).
- d) **Chak 4Q:** The total CCA of the Chak is 322.33 ha, and the effective CCA considered under the CADWM Project is 155.49 ha. The construction work is completed, and the water course has been handed over to the WUA. The total length of water courses is 7463.03 meters, of which 3288.79 meters have been constructed under this scheme

A meeting was held in the office of the ACE, CAD, Bikaner, which was attended by the ACE (CAD), Superintending Engineers of Bikaner and Sri Ganganagar, and Executive Engineers and Assistant Engineers of the CAD Departments. During the meeting, the issue of slow progress in the disbursement of Functional Grants was discussed and concerns were raised over non-utilization of token CA so far. The status of the CA proposal for FY 2026–27 and the latest revised MoU, under which the project is scheduled for completion by March 2027, was also reviewed. Subsequently, during the site visit, discussions were held with the Executive Engineer and other field officers of the CAD regarding the progress of works. Interactions were also conducted with members of the Water Users Associations (WUAs). The following officers of the State Government participated in the monitoring visit.

S. No	Name of Officer	S. No	Name of Officer
a)	Shri Mool Singh, ACE	b)	Shri Mahesh Parewa SE CAD, BKN
c)	Shri Nirajan Lal Meena, SE, SGR	d)	Shri Arvind Agrawal, SE, BKN
e)	Shri Neeraj Kumawat, EE, SGR	f)	Shri Subhash Badhala, EE, BKN
g)	Shri Ajay Kumar Saini, AEN, BKN		Other Officers and Staff of WRD, GoR

ANNEXURE-IV

GOVERNMENT OF RAJASTHAN COMMAND AREA DEVELOPMENT

Annexure-II (Proforma-3)
(Area in Th Ha)

PHYSICAL PROGRESS OF THE PROJECT - GANG CANAL PROJECT PHASE-II

State	Rajasthan	District	Sri Ganganagar	CADA	Area Development Commissioner, BIKANER
PROJECT- GANG CANAL PROJECT PHASE-II					
1	CCA			44.875 (modified to 117.975)	
2	UIP			35.451 (Modified to 93.200)	
3	Irrigation potential -			44.875 (modified to 117.975)	
		a) Created during 2022-23 (LFY)		Already created	
		b) Utilized during 2022-23 (LFY)		Already created.	
		c) Created upto the 2025-26 (LFY) Under CADP		112.353	
		d) Utilised up to 2025-26 (LFY) Under CADA		112.353	
4	Category of the project			General	
5	Year of inclusion under CADWM			2015-16	

SN	ACTIVITY	TOTAL QUANTAM OF WORK INVOLVED (000 HIA)	CUMMULATIVE ACHIEVEMENT UPTO BEGINNING OF 2025-26 (LFY)	TARGET & ACHIEVEMENT FOR 2025-26 (LFY)		CUMMULATIVE ACHIEVEMENT UPTO END OF 2025-26 (LFY)	TARGETS & ACHIEV. FOR 2026-27 (CFY)			Reasons/ Justification for shortfall
				TARGETS	ACHIEVEMENTS		TARGETS for the year 2026-27	ACHIEVEMENTS (iii) 31.03.2026	TARGETS FOR REMAINING PERIOD	
1	2	3	4	5	6	7	8	9	10	11
A	Structural Intervention									
a)	Survey, Planning and Design	117.975	109.06	8.915	3.638	112.698	5.277	0	5.277	Extension of the MoU was awaited
b)	OFD Works (Comprising of construction of field channels micro-irrigation, land leveling / shaping wherever necessary)									1. Delay in payment of work done due to delayed release of credit limit by GOR in the month of Jan 19 after month of March 19, 2. Boycott of tenders by

i) Total area of Lined Channels (underground pipelines) (in Th ha)	117.975	103.467	14.508	8.886	112.353	5.622	0	5.622	contractor for six months. 3. Lockdown due to COVID 19 in 2020-21 4. Delay in approval of MoU in 2022-23 5. Delay in release of CA instalments
(ii) Area under mechanised leveline / laser leveling	-	-	-	-	-	-	-	-	
(iii) Area under Micro-Irrigation (with grid power/ solar panel and pump) wherever possible.									The cultivators and Wuas have been using flow irrigation system of irrigation since past 70-80 years and are habiyual of it. They are not allowing the micro irrigation system in small areas and therefore provion of minimum 10% CCA with MI have been approved by CWC and MoWRRD&GR, Gol, New Delhi in 2019-20.
(iii) (a) Infrastructure (Grid power)	0	0	0	0	0	0	0	0	
(iii) (b) Infrastructure (Solar Equipments)	0	0	0	0	0	0	0	0	
SubTotal (iii)	0	0	0	0	0	0	0	0	
c) Construction of field,	-	-	-	-	-	-	-	-	
d) Correction of system	-	-	-	-	-	-	-	-	
e) Reclamation of waterlogged area	-	-	-	-	-	-	-	-	
(i) No. of schemes approved by	-	-	-	-	-	-	-	-	
(iii) Area reclaimed	-	-	-	-	-	-	-	-	
-Surface drainage/ bio drainage	-	-	-	-	-	-	-	-	
-Sub-Surface drainage	-	-	-	-	-	-	-	-	
B Non-Structural Interventions									
f) One time functional/ infrastructure grant to registered WUAs	-	-	-	-	-	-	-	-	Survey being taken up
(i) One Time Functional Grant	117.975	21.037	96.938	45.368	66.405	51.570	0	51.570	
(i) No. of WUAs registered	180	180	0	0	180	0	0	0	Already formed and functioning

(i) Area covered under the WUAs	314.268	314.268	0	0	314.268	0	0	0
(iii) No. of WUAs which have been handed over the system	180	180	0	0	180	0	0	0
(iv) Area Covered	314.268	314.268	0	0	314.268	0	0	0
(II) Infrastructure Grant								
(i) No of WUAs	-	-	-	-	-	-	-	-
(ii) Area covered under the WUAs	-	-	-	-	-	-	-	-
g) (A) Adaptive Trials	-	-	-	-	-	-	-	-
(i) No of Trials	-	-	-	-	-	-	-	-
(ii) Area Covered	-	-	-	-	-	-	-	-
(B) Demonstration Programmes								
(i) No of Plots								
(ii) Area covered								
(iii) Mechanised /laser land leveling (Nos.)	-	-	-	-	-	-	-	-
(iv) Micro-Irrigation (Nos)	-	-	-	-	-	-	-	-
(v) Water use efficiency (Nos.)	-	-	-	-	-	-	-	-
(C) State Level trainings	-	-	-	-	-	-	-	-
(i) No. of Officials Trained	-	-	-	-	-	-	-	-
(ii) No. of Farmers trained	-	-	-	-	-	-	-	-
(D) Monitoring and Evaluation studies conducted by the State	-	-	-	-	-	-	-	-

Not included in the scope of work in the approved DPR

Yes, (1) through Director (M&A), CWC, Jaipur and (2) Through Director of Evaluation, GoR, Jaipur (in progress)

Sudhakar
Executive Engineer (D-III)
CAD, Bikaner

2/5/17
Superintending Engineer
O/o ACE, CAD, Bikaner

[Signature]
Additional Chief Engineer (West)
CAD, Bikaner

Name of the CAD Project

GOVERNMENT OF RAJASTHAN
COMMAND AREA DEVELOPMENT
GANG CANAL PROJECT PHASE-II

Financial Data

ANNEXURE-VII (Proforma-2)

1 Estimated cost as per District Irrigation Plan (DIP) under CADWM Programme Rs 341.53 Crore

Expenditure incurred so far (Audited) - 1176.36 + 1299.20 + 1485.01 + 2875.70 + 6625.31 + 8354.06 + 3844.39 + 2851.18 + 2098.92 + 2568.34 Lacs = 33178.47 Lacs (Rs 30495.24

2 excluded establishment expenditure rs 2683.23 lacs in State fund which is borne Central Share 50% State Share 50% Total 100% by GOR)

3 Balance Expenditure to be incurred

RS 3657.76 LACS

4 Budget Provision for 2026-27 (CFY) Additional budget demanded to FD GOR

2100.00

Amount in Rs Lacs

SN	ITEM	MOTHER SANCTION Released during 2025-26	Exp. during F.Y. 2025-26			Exp. during F.Y. 2026-27		
			State Share	Central Share	Total	State Share	Central Share	Total
1	2	3	4	5	6	7	8	9
A.	Structural Interventions:							
a)	Survey, Planning and Designing of OFD works		0.00	0.00	0.00	0.00	0.00	0.00
b)	OFD works (Comprising of construction of field channels, micro-irrigation, land levelling/shaping wherever necessary)		0.00	0.00	0.00	0.00	0.00	0.00
	i) Construction of field channel/Underground pipelines		1059.35	1059.35	2118.70	0.00	0.00	0.00
	ii) Mechanised land leveling in the hilly/difficult areas, laser levelling in selected areas, wherever applicable		0.00	0.00	0.00	0.00	0.00	0.00
	iii) Micro-irrigation (infrastructure with grid power/solar panel and pump, wherever possible.		0.00	0.00	0.00	0.00	0.00	0.00
	iii)(a) Grid Power		0.00	0.00	0.00	0.00	0.00	0.00
			0.00	0.00	0.00	0.00	0.00	0.00
	iii)(b) Solar power/equipment		0.00	0.00	0.00	0.00	0.00	0.00
			0.00	0.00	0.00	0.00	0.00	0.00
	Sub Total (iii)		0.00	0.00	0.00	0.00	0.00	0.00
c)	Field, intermediate and link drains		0.00	0.00	0.00	0.00	0.00	0.00
d)	Correction of conveyance system deficiencies above outlet upto distributaries 4.25 cumec(150 cusec) capacity	1287.90	0.00	0.00	0.00	0.00	0.00	0.00
e)	Reclamation of waterlogged areas		0.00	0.00	0.00	0.00	0.00	0.00
B	Non- Structural Interventions		0.00	0.00	0.00	0.00	0.00	0.00
f)	One time functional grant for WUAs. Total amount deposited as Fixed deposit in the		224.82	224.82	449.64	0.00	0.00	0.00
	(i) Functional Grant		0.00	0.00	0.00	0.00	0.00	0.00
	(ii) Infrastructural Grant		0.00	0.00	0.00	0.00	0.00	0.00
g)	(i) Adaptive trials		0.00	0.00	0.00	0.00	0.00	0.00
	(ii) Demonstrations (including on		0.00	0.00	0.00	0.00	0.00	0.00
	(iii) Training courses organised by the State		0.00	0.00	0.00	0.00	0.00	0.00
	(iv) Monitoring and Evaluation studies		0.00	0.00	0.00	0.00	0.00	0.00
	(v) Action Research		0.00	0.00	0.00	0.00	0.00	0.00
	Sub total (g)		0.00	0.00	0.00	0.00	0.00	0.00
	Allocation/Expenditure on SC and ST farmers out of total grant		0.00	0.00	0.00	0.00	0.00	0.00
h)	Establishment cost		0.00	0.00	0.00	0.00	0.00	0.00
	(i) Estt. Cost of State headquarters		0.00	0.00	0.00	0.00	0.00	0.00
	(ii) Estt. Cost of CADAs/ projects		0.00	0.00	0.00	0.00	0.00	0.00
	TOTAL EXPENDITURE		1284.17	1284.17	2568.34	0.00	0.00	0.00

Chief Accounts Officer
CAD (West), Bikaner

ACE CAD(West)
Bikaner


SCALE:- 1 CM = 165



HYDRAULIC DATA:-

LEGEND

KEY PLAN



CERTIFICATE:-

1. The area of adjoining checks has been compared and found correct. There is no omission of land.
2. The check scheme has been prepared as per design manual and other norms laid down in it. The check plan envisages minimum waste length of use with maximum irrigation efficiency.
3. The existing filling proposed in A Section is unavoidable. 4. No area is de-committed which is already irrigated. 5. Restia, Road, Abdul, nursery are marked as per record of Revenue / W.R. Department. 6. Alignment of cut has been examined & checked by E.E as proposed in Check Plan. 7. FSL of parent channel is as per existing FSL by channel & checked at site. 8. There is no hard pan / gypsum in command area.
9. Soil is suitable for irrigation. 10. Existing FSL of off take points and tails of all laterals & m/c has been checked by me. 11. Length of damaged m/c has been checked by me. 12. The length of already constructed / raising / repairing has been checked by me.
13. Previous length constructed / required modification / raising / repairing has been checked by me.

(विनाल बुनार नगी)
बहराक नगीदना
गंगज अरुपकी उरक दान (अ=६६६)
रि. ६ डि. बुनार

24/1/24
(राजकुमार सिंगल)
अविवाही अभियन्ता
मंगनर ओ० एफ० वी० एच०-६
सि० षे० पि०, सूरतगढ़

PREPARED BY

SUBMITTED BY

RECOMMENDED BY

APPROVED BY

Dr


(विशाल कुमार वर्मा)
सहायक अभिदन्ता

राजकुमार सिंघल)

2000
(सामानाचार्य गोपरी)


GOVERNMENT OF KAZAKHSTAN
GANG CANAL PROJECT

COMMAND AREA DEVELOPMENT
CHAK PLAN OF CHAK 76 LNP

[illegible][illegible]

NEW PLAN

KEY PLAN

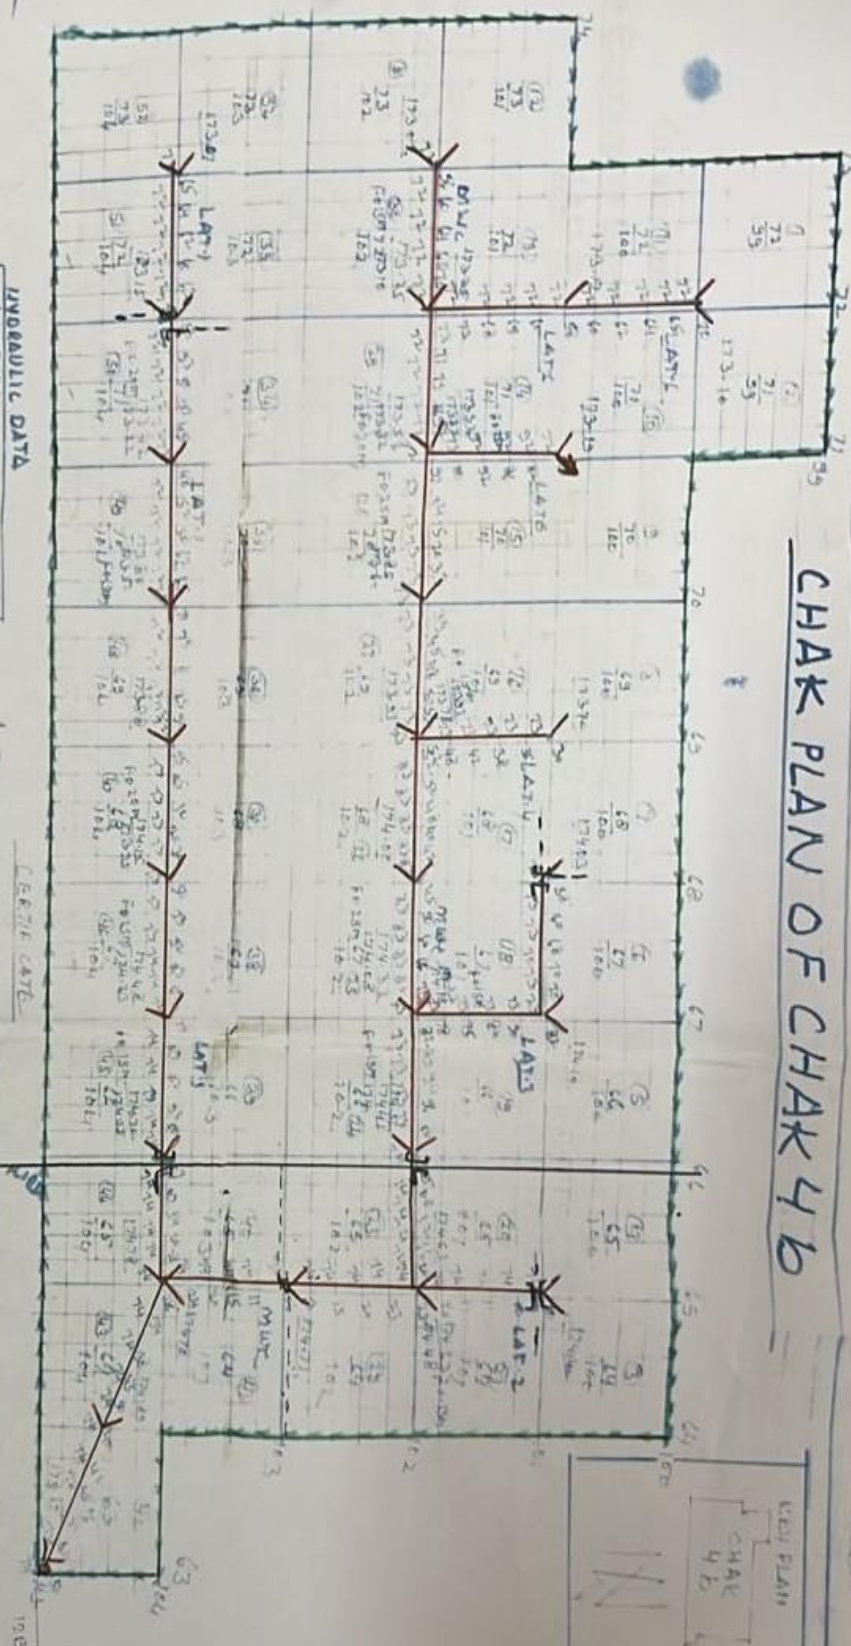

HYDRAULIC DATA

4435.76

175 2/10
175 2/10

134150
166 732 7100 W781

WICKINGHEAD
WATER ALLIANCE

DISCHARGE
25000

卷之四

UCLA IN HA
/ 000 IN HA

Grading work

LENGUJA SHQIPTARE
TE DE LUFTES 770336

UNLINED

672706 7703-300

4. 3. 11. 2. 1.

—

1

[illegible]

GOVERNMENT OF KARNATAKA GRAMODAYA DEVELOPMENT GAWA MANAAR PROJECT CHIKHEANDE HALL 4 b 21-2-2007 (for copy) subject: agreement	RECEIVED BY 21-2-2007 (for copy) subject: agreement
RECEIVED BY 21-2-2007 (for copy) subject: agreement	RECEIVED BY 21-2-2007 (for copy) subject: agreement

CHAK PLAN OF CHAK 4-Q.

KEY PLAN

LEGEND

- CHAK BOUNDARY
- WATER ALREADY LINED
- ROAD TO BE LINED
- CHAKS KACHALD
- KACHALD
- NAKA POINT
- OUTLET POINT
- ROAD PLCC
- RASHTA KUBT
- CHUNGRT
- UNI COMMON
- ROAD

CARNATION

1. The area of adjoining Chak has been compared and found correct.

1 The area of Navigation Chart has been compared and found correct
2 There is no change of limit
3 The chart area has been checked as per details of material and other markings
4 laid down in the plan of the Chart. The chart plan indicates minimum work
5 to be done with minimum Navigation equipment
6 Navigation plan of the Chart is as follows:
7 1. Area of the Chart is as follows:
8 2. Area of the Chart is as follows:
9 3. Area of the Chart is as follows:
10 4. Area of the Chart is as follows:
11 5. Area of the Chart is as follows:
12 6. Area of the Chart is as follows:
13 7. Area of the Chart is as follows:
14 8. Area of the Chart is as follows:
15 9. Area of the Chart is as follows:
16 10. Area of the Chart is as follows:
17 11. Area of the Chart is as follows:
18 12. Area of the Chart is as follows:
19 13. Area of the Chart is as follows:
20 14. Area of the Chart is as follows:
21 15. Area of the Chart is as follows:
22 16. Area of the Chart is as follows:
23 17. Area of the Chart is as follows:
24 18. Area of the Chart is as follows:
25 19. Area of the Chart is as follows:
26 20. Area of the Chart is as follows:
27 21. Area of the Chart is as follows:
28 22. Area of the Chart is as follows:
29 23. Area of the Chart is as follows:
30 24. Area of the Chart is as follows:
31 25. Area of the Chart is as follows:
32 26. Area of the Chart is as follows:
33 27. Area of the Chart is as follows:
34 28. Area of the Chart is as follows:
35 29. Area of the Chart is as follows:
36 30. Area of the Chart is as follows:
37 31. Area of the Chart is as follows:
38 32. Area of the Chart is as follows:
39 33. Area of the Chart is as follows:
40 34. Area of the Chart is as follows:
41 35. Area of the Chart is as follows:
42 36. Area of the Chart is as follows:
43 37. Area of the Chart is as follows:
44 38. Area of the Chart is as follows:
45 39. Area of the Chart is as follows:
46 40. Area of the Chart is as follows:
47 41. Area of the Chart is as follows:
48 42. Area of the Chart is as follows:
49 43. Area of the Chart is as follows:
50 44. Area of the Chart is as follows:
51 45. Area of the Chart is as follows:
52 46. Area of the Chart is as follows:
53 47. Area of the Chart is as follows:
54 48. Area of the Chart is as follows:
55 49. Area of the Chart is as follows:
56 50. Area of the Chart is as follows:
57 51. Area of the Chart is as follows:
58 52. Area of the Chart is as follows:
59 53. Area of the Chart is as follows:
60 54. Area of the Chart is as follows:
61 55. Area of the Chart is as follows:
62 56. Area of the Chart is as follows:
63 57. Area of the Chart is as follows:
64 58. Area of the Chart is as follows:
65 59. Area of the Chart is as follows:
66 60. Area of the Chart is as follows:
67 61. Area of the Chart is as follows:
68 62. Area of the Chart is as follows:
69 63. Area of the Chart is as follows:
70 64. Area of the Chart is as follows:
71 65. Area of the Chart is as follows:
72 66. Area of the Chart is as follows:
73 67. Area of the Chart is as follows:
74 68. Area of the Chart is as follows:
75 69. Area of the Chart is as follows:
76 70. Area of the Chart is as follows:
77 71. Area of the Chart is as follows:
78 72. Area of the Chart is as follows:
79 73. Area of the Chart is as follows:
80 74. Area of the Chart is as follows:
81 75. Area of the Chart is as follows:
82 76. Area of the Chart is as follows:
83 77. Area of the Chart is as follows:
84 78. Area of the Chart is as follows:
85 79. Area of the Chart is as follows:
86 80. Area of the Chart is as follows:
87 81. Area of the Chart is as follows:
88 82. Area of the Chart is as follows:
89 83. Area of the Chart is as follows:
90 84. Area of the Chart is as follows:
91 85. Area of the Chart is as follows:
92 86. Area of the Chart is as follows:
93 87. Area of the Chart is as follows:
94 88. Area of the Chart is as follows:
95 89. Area of the Chart is as follows:
96 90. Area of the Chart is as follows:
97 91. Area of the Chart is as follows:
98 92. Area of the Chart is as follows:
99 93. Area of the Chart is as follows:
100 94. Area of the Chart is as follows:
101 95. Area of the Chart is as follows:
102 96. Area of the Chart is as follows:
103 97. Area of the Chart is as follows:
104 98. Area of the Chart is as follows:
105 99. Area of the Chart is as follows:
106 100. Area of the Chart is as follows:

नेहरून
 (आपुन १९५५)
 अनिष्ट अनिष्टता

John
 [Signature]

ॐ

CHAKRIAN OF CHAKRIAN
PREPARED BY SUBMITTING

१५२२
(आधुनिक रूप)
कनिष्ठ आचार्य

(अध्यापक सुभाष चन्द्र)
सहायक अध्यापक
संगीत (अध्यापक-5)
वि.सं.वि., बी.सं.वि.

12.6.24

APPENDIX A

21/11/2019

(१०७)

PHOTOGRAPHS

CAD&WM WORKS

Chak 76 LNP



10 Q II





4 B







Chak 4 Q





Meeting



PART-III SUMMARY OF ACTIONABLE POINTS

3.1 CAD&WM WORKS:

1. The physical progress under different activities of the project is not being achieved as per year wise targets fixed in the last MoU signed for the project. Further, there is negligible progress in non-Structural portion of the project. Functional grant has been distributed only for 66405 Ha out of 117975 Ha upto March 2025.
2. It is advised to have all the field channels in the command to be marked in GIS layers to have holistic view of the coverage of complete command.
3. As per clause 14 of the latest MoU, Independent evaluation of the project is mandatory and shall be carried out by State Govt through an independent agency and report shall be submitted to CWC/Ministry. State Govt. is requested to submit the report of independent evaluation.
4. As per the latest Revised MoU, total cost of the project is fixed at Rs 328.062 Cr for covering CCA of 117975 Ha by Mar-2027. Eligible expenditure up to 31.03.2026 is Rs 304.95 Cr crore with physical progress of 112353 Ha. In the CA proposal, Plan for 2026-27 has been kept for covering balance CCA of 5622 Ha with an estimated cost of Rs 22.31 Cr. Central assistance for FY 2026-27 has been calculated considering ceiling cost of project as 328.062 Cr as per latest Revised MoU. Cost over and above the ceiling cost (Rs 328.062 Cr) if any shall be entirely borne by the states as per Clause 4.4 of the “Guidelines for Central Assistance for Command Area Development Works in Prioritized AIBP Funded Irrigation Projects” for completion of the project.
5. State government should ensure additional funds from State Budget for expenditures over and above the ceiling cost for completion of project (CCA-117975 Ha).
6. Ceiling of establishment cost had been fixed at 10 percent of OFD works as per CADWM guidelines.
7. Functional Grant disbursement is behind schedule. Structural and Non-Structural interventions should be accelerated to achieve project completion by March 2027 as committed in the revised MoU of GoR.

भारत सरकार
जल शक्ति मंत्रालय
जल संसाधन नदी विकास एवं गंगा संरक्षण विभाग
केंद्रीय जल आयोग
प्रबोधन एवं मूल्यांकन निदेशालय



Government of India
Ministry of Jal Shakti
Dept. of Water Resources, RD&GR
Central Water Commission
Monitoring & Appraisal Directorate

सेवा में,

वरिष्ठ संयुक्त आयुक्त-(SPR-II)
जल संसाधन, नदी विकास एवं गंगा संरक्षण विभाग
जल शक्ति मंत्रालय
नई दिल्ली ।

विषय: CADWM योजना की 99 प्राथमिक प्रोजेक्ट के तहत गंगनहर परियोजना फेज- द्वितीय के लिए संसोधित MoU भिजवाने बाबत ।

संदर्भ - 1. Letter No. प.4 (14)सीएडी/2014-00009 दिनांक 29.05.2024
2. Letter No. F-118/GCP-II/ CADB/D&M/2024-26/263 dated 16.07.2024

कृपया मुख्य शासन उप सचिव सीएडी, राजस्थान सरकार जयपुर के इस कार्यालय को संबोधित पत्र क्रमांक प.4 (14)सीएडी/2014-00009 दिनांक 29.05.2024 का संज्ञान ग्रहण करें जिसमें CADWM योजना की 99 प्राथमिक प्रोजेक्ट के तहत गंगनहर परियोजना फेज- द्वितीय की MoU दिनांक 01.04.2024 से 31.03.2026 तक बढ़ाए जाने के क्रम में अतिरिक्त मुख्य सचिव द्वारा हस्ताक्षरित MoU आवश्यक कार्यवाही हेतु प्रेषित की गयी है । संदर्भ -2 दिनांक 16.07.2024 के माध्यम से अतिरिक्त चक जो की ईस MoU द्वारा जोड़े गए हैं, के विषय में मुख्य अभियंता CAD, बीकानेर द्वारा Clarification प्रस्तुत किया गया है।

Revised MoU has been examined in this office and the observations/comments of this office are as under:

- As per last MoU (01.04.2022) 538 no.s of Chaks had been considered with total CCA of 117975 Ha. Out of 538 Chaks, 14 chaks having total CCA of 1147 Ha is proposed to be deleted and also net saving in CCA of 6933 ha in the rest of chaks has been conveyed by state authorities. A total saving of 8080 Ha has been informed by state authorities.
- In the proposed MoU (2024-2026), 41 similar old outlets/Chaks of the Gang system having total CCA of 8080 Ha has been proposed to be included in the scheme, keeping total CCA under the scheme as 117975 Ha. Upon examination of the list (Annex-A) of the proposed 41 Chaks, the following has been observed:

No. of Chaks	Cost Incurred (Rs in Lakhs)	Status
8	630	Already Completed (2018-2024)
7	-	Works in Progress

File No.T-56039/13/2019-MA JAIPUR

13	-	Under Tendering Process
13	-	Not started.

Works in 8 no.s of Chaks has already been completed incurring expenditure of Rs 6.3 Cr before inclusion in scheme/before approval of competent authority. Further for 7 No. of chaks, works are already in progress and for 13 No. of Chaks works are under tendering process.

- c. The total nos of Chaks gets revised from 538 to 565 (538-14+41) in the proposed MoU. Further the estimated cost has also been proposed to be revised from Rs 341.534 Cr to Rs 340.841Cr.

The revised MoU along with above observations/comments are forwarded for further necessary action please.

उक्त पत्र मुख्य अभियंता, यमुना बेसिन संगठन नई दिल्ली के अनुमोदन से जारी किया जा रहा है।

भवदीय

अभिषेक गुप्ता
अभिषेक गुप्ता 25/7/24
निदेशक

संलग्नक: यथोक्त

प्रतिलिपि सूचनार्थ :

- 1) अतिरिक्त मुख्य सचिव (ACAD & WM), राजस्थान सरकार , जयपुर
- 2) आयुक्त (SPR), जल संसाधन, नदी विकास एवं गंगा संरक्षण विभाग, जल शक्ति मंत्रालय, नई दिल्ली।
- 3) आयुक्त (CAD), जल संसाधन, नदी विकास एवं गंगा संरक्षण विभाग, जल शक्ति मंत्रालय, नई दिल्ली।
- 4) मुख्य अभियंता, यमुना बेसिन संगठन, केंद्रीय जल आयोग, नई दिल्ली।
- 5) मुख्य अभियंता, परियोजना प्रबोधन संगठन, केंद्रीय जल आयोग, नई दिल्ली।
- 6) मुख्य अभियंता एवं अतिरिक्त सचिव (CAD), राजस्थान सरकार, जयपुर।

कमरा सं 107, खंड-ए, केन्द्रीय सदन
विद्याधर नगर, जयपुर-302039
दूरभाष: 0141-2030154/2944007
ईमेल: dirmajaipur-cwc@nic.in

♣ जल संरक्षण-सुरक्षित भविष्य, ♣



Room No. 107, Wing-A,
KendriyaSadanVidhyadhar Nagar, Jaipur-
302039

Tel: 0141-2030154/2944007

email: dirmajaipur-cwc@nic.in

♣ Conserve Water- Save Life ♣

राजस्थान सरकार
कार्यालय मुख्य अभियंता (पश्चिम) सीएडी, बीकानेर

क्रमांक:- F 103/ CWC/D&M/ 826
अधीक्षण अभियंता
ओएफडी वृत्त
बीकानेर।

दिनांक :- 29/12/2023

विषय:-केन्द्रीय जल आयोग, जयपुर के अधिकारियों द्वारा CADWM कार्यों के मूल्यांकन हेतु क्षेत्रीय दौरा करने बाबत।

प्रसंग- केन्द्रीय जल आयोग जयपुर का पत्रांक T-56039/7/2019-MA JAIPUR Part(2) दिनांक 28.12.2023

महोदय,


उपरोक्त विषयान्तर्गत निर्देशानुसार लेख है कि केन्द्रीय जल आयोग जयपुर के अधिकारियों द्वारा इस संगठन के क्षेत्राधिकार के अन्तर्गत CADWM योजना अन्तर्गत गंगकेनाल फेज द्वितीय के निर्मित/निर्माणाधीन कार्यों के मूल्यांकन हेतु दिनांक 02.01.2024 से 04.01.2023 तक निरीक्षण किया जाना प्रस्तावित है। (प्रति संलग्न) इस हेतु आपको नोडल अधिकारी नियुक्त करते हुए निर्देशित किया जाता है कि आप CADWM कार्यों से संबंधित क्षेत्रीय भ्रमण/कार्यालय रिकार्ड आदि सहित सम्पूर्ण तैयारियों के साथ केन्द्रीय जल आयोग जयपुर के अधिकारियों को सहयोग प्रदान करें। तथा इस संबंध में केन्द्रीय जल आयोग के अधिकारी श्री साकेत कृष्ण उपनिदेशक (मोबाईल नं० 8800155634) से सम्पर्क कर सम्पूर्ण कार्यक्रम की जानकारी प्राप्त करने का श्रम फरमावें।


अधीक्षण अभियंता(प्रशासन)
01/ कार्यालय मुख्य अभियंता (पश्चिम)
सीएडी बीकानेर

क्रमांक:- F 103/ CWC/D&M/ 827-28
प्रतिलिपि -

दिनांक :- 29/12/2023

1. श्रीमान निदेशक केन्द्रीय जल आयोग जयपुर को भेजकर निवेदन है कि प्रस्तावित विजिट से संबंधित व्यवस्था हेतु इस संगठन के अधीक्षण अभियंता ओएफडी वृत्त, बीकानेर श्री हेमराज कोली (मो० न० 9829072108) से सम्पर्क स्थापित करने का श्रम करें।
2. अधीक्षण अभियंता सीएडी वृत्त हनुमानगढ़ व अधीक्षण अभियंता ओएफडी वृत्त श्रीगंगानगर एवं अधीक्षण अभियंता फील्ड टेस्टिंग एवं गुण नियंत्रण वृत्त सूरतगढ़ को निर्देशित किया जाता है कि आप अपने अधीनस्थ अधिकारियों को निर्देश फरमावें कि वे CADWM कार्यों से संबंधित क्षेत्रीय भ्रमण/कार्यक्रम में केन्द्रीय जल आयोग के अधिकारियों को सम्पूर्ण रिकॉर्ड सहित सहयोग करें तथा इस हेतु श्री हेमराज कोली से सम्पर्क स्थापित करें।


01/ अधीक्षण अभियंता(प्रशासन)
